



ASOIF General Assembly LA28 Update

27 May 2026



Sport



Our What & When

Venues



Our Where & How

Stakeholders



Our Who & Why

LA28 GAMES BY THE NUMBERS



THE LA28 CHALLENGE:

*To develop the most
complex site & operational plans*

*that will deliver
the largest
Sport program*

in the history of
**THE OLYMPIC AND
PARALYMPIC GAMES**

36
OLY IFs/SPORTS

353
Medal Events

11,198
OLY ATHLETES

50
COMP VENUES

7
MAJOR NON-COMP
VENUES

40
OTHER NON-COMP
VENUES

22
VENUE CITIES

60
DAYS OF OPERATION

841
Ticketed Sessions

Highlights & Key Progress



International Federations

IF Visits
ORIS Meetings
Qualification



National Olympic & Paralympic Committees

Individual Visits
Open Days
Early Allotment Agreements



Press & Media

Preparation for World Press Briefing
& World Broadcaster Meeting



Competition Schedule

Olympics by event
Paralympics by event (NEW)



Venue Plan Updates

Announced Remote Football Cities
Confirmed Road Cycling & TT Finish
Confirmed Para Road Cycling
Announced Olympic Village OKC



Event & Venue Operational Planning

Launched EOP2
Integration of Sport & EVM
Launched VIG, VOC, Change Management



Venue Design Books & Procurement


Published VDB 3.0
Path to VDB 3.1



Event Testing

Shared Event Testing Calendar
with International Federations

Testing and Readiness Activities

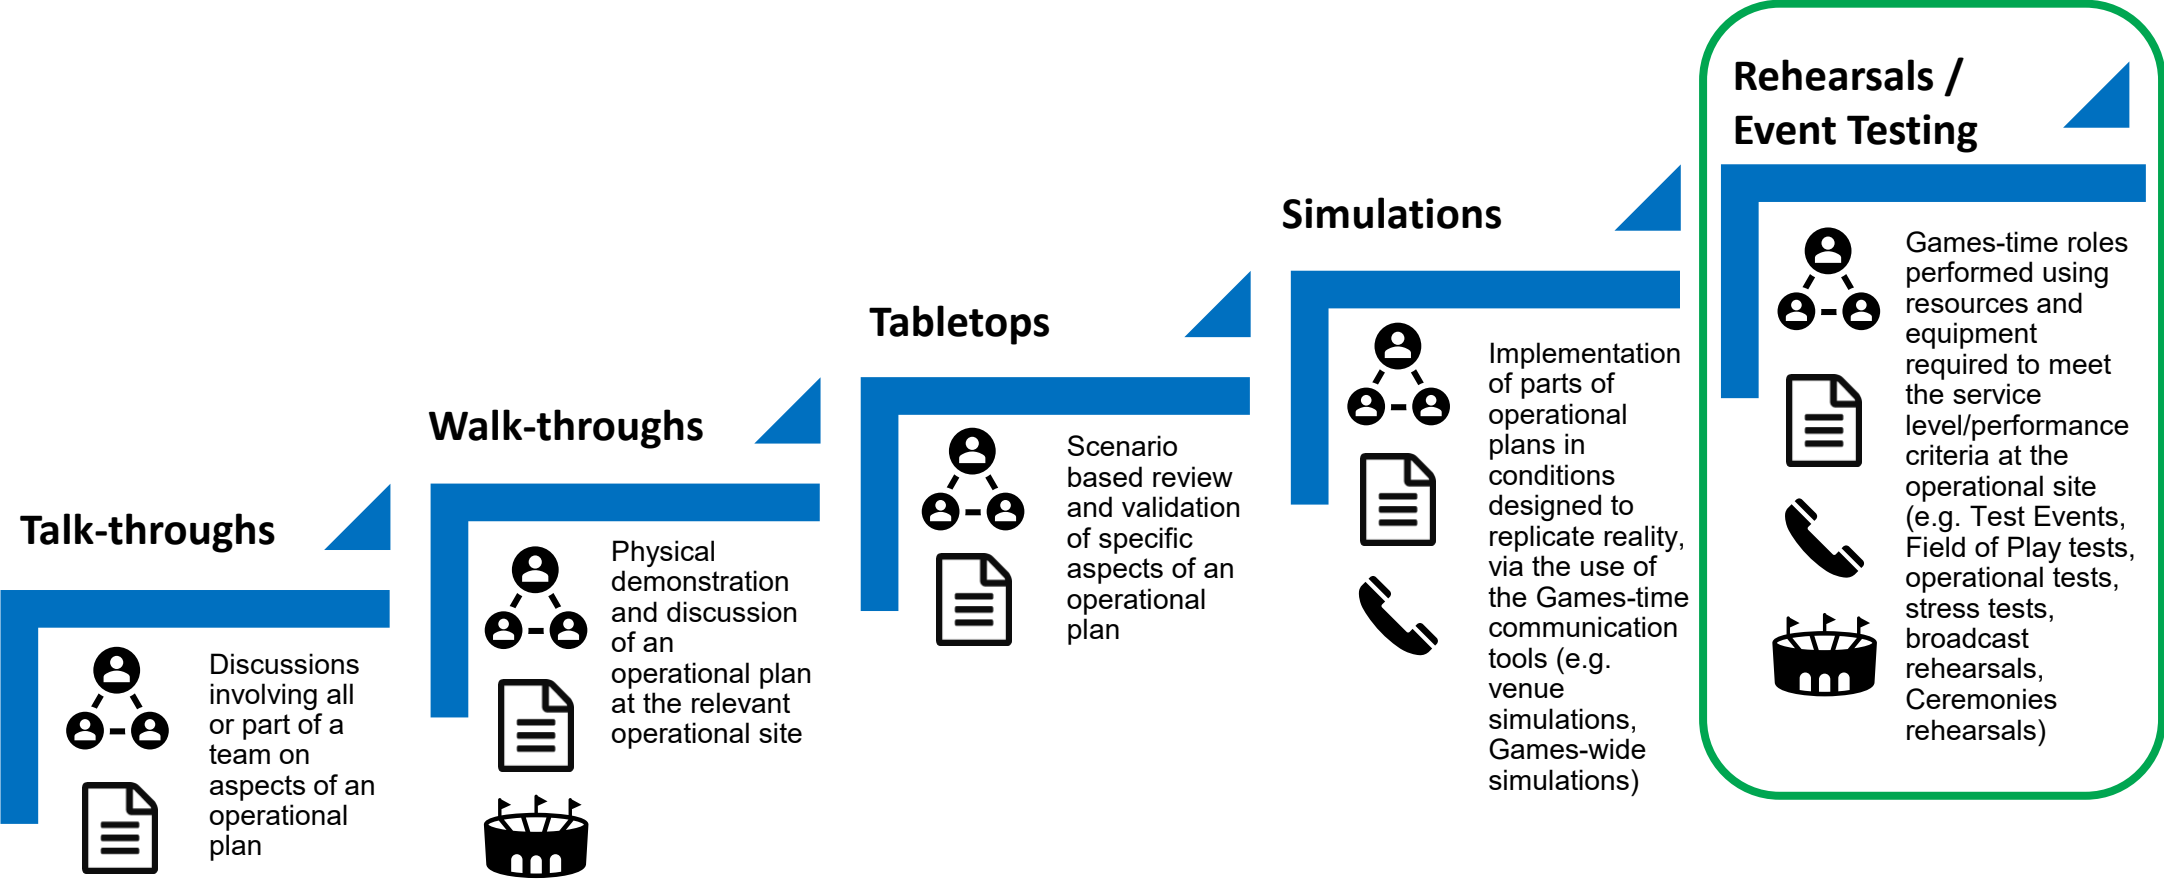

Provides opportunities for Team building and additional training

Testing Strategy



OBJECTIVE Deliver selective, risk-based Event Testing (ET) to validate Games-time readiness across sports, venues, systems, and workforce.

1 APPROACH

Risk Assessment Across four
main functional areas

Sport: athlete safety, competition fairness, weather impact, FOP installation/operation, workforce training

Technology: venue/FOP technology complexities, TSR risks

Venue Infrastructure & Event Management: build time and complexity, venue flows and concurrence of activities

2 SCOPE/TIMING

Event Testing includes
competitions and other testing
activities

Wave 1: Q3 2027

Wave 2: Q4 2027 – Q1 2028

Wave 3: Q2 2028

3 OWNERSHIP


3 approaches to
ownership

LA28 fully owned testing/events


Co-owned/delivered testing/events between LA28 and 3rd party (IF, NGB, Pro-League)

3rd party owned/delivered events

LA28 Staffing Update

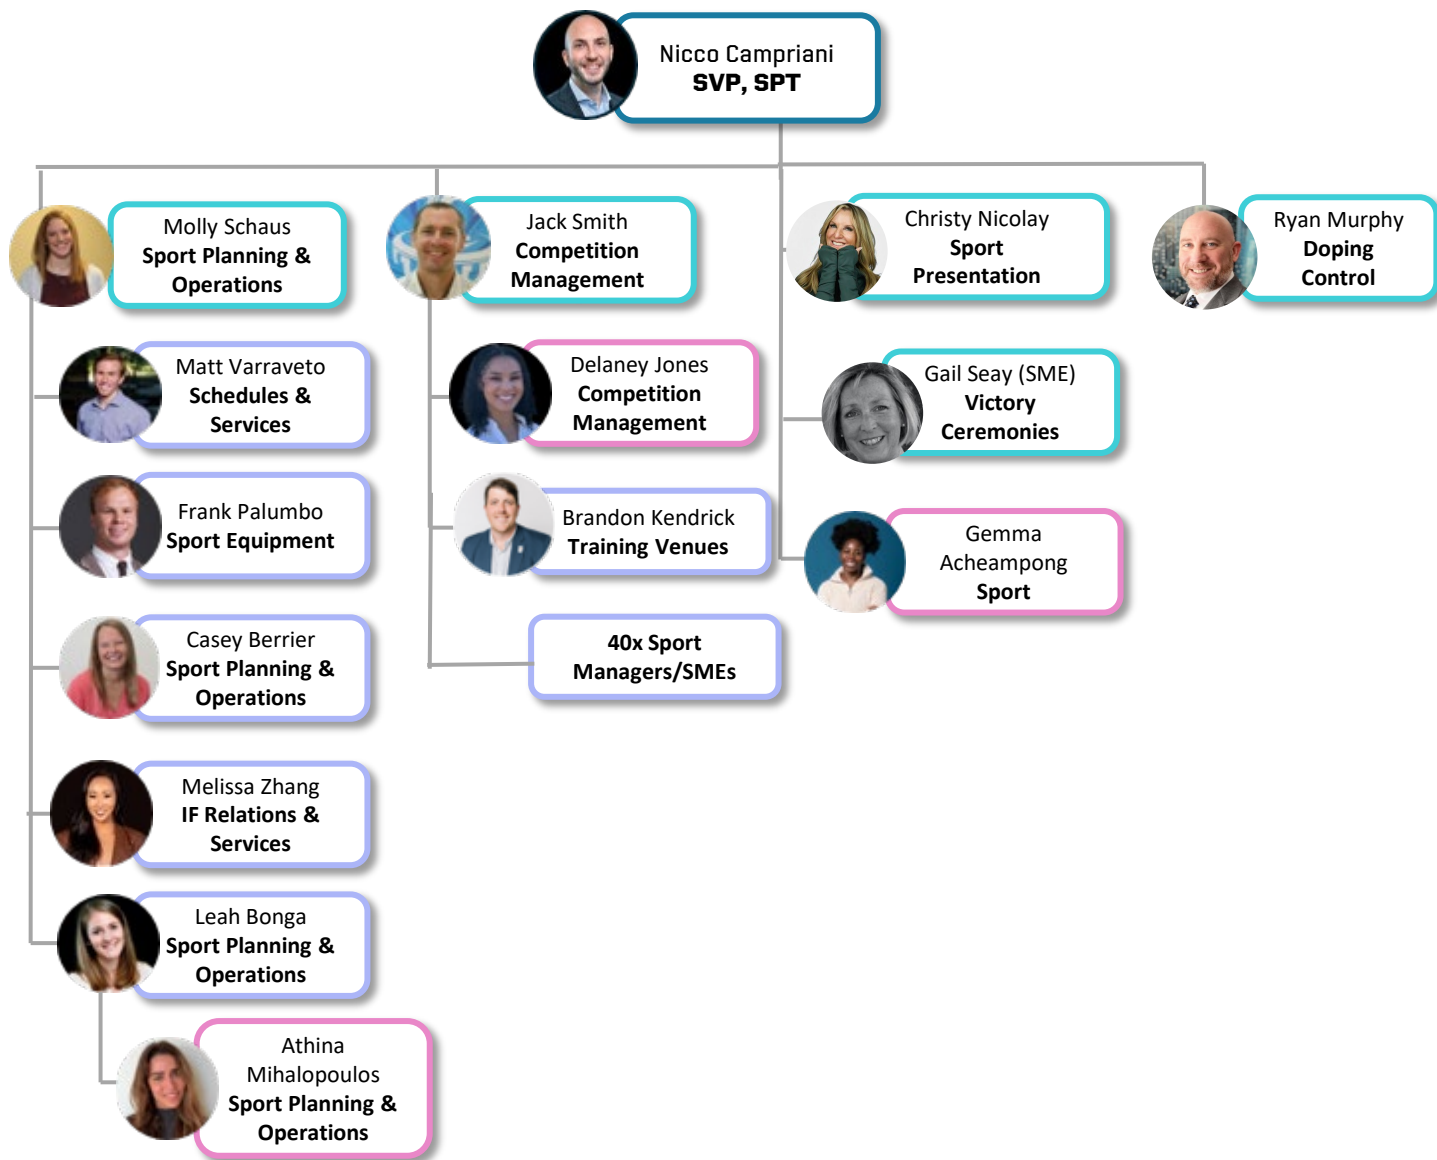

Generic Sport Structure per Discipline

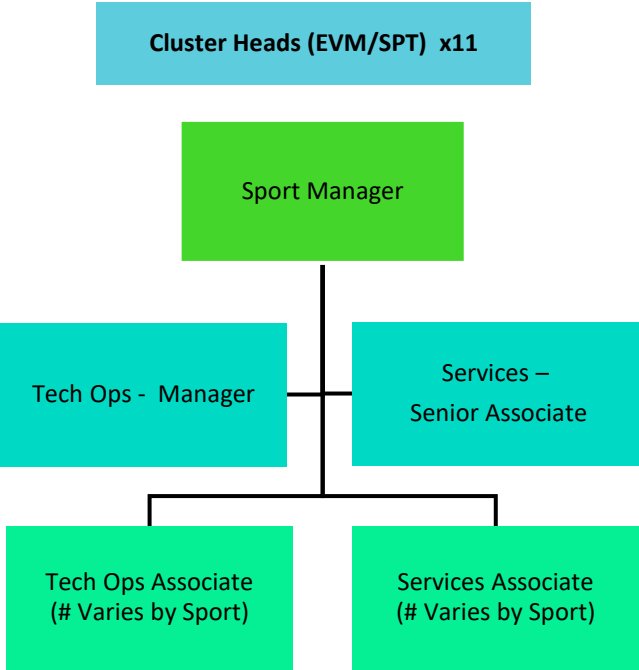

LA28 Staffing Update



- EVM | SPT merge complete with (11) Cluster Leads
- (34) Sport Managers + (6) Subject Matter Experts onboarded, dedicated coverage or hired/identified candidate across all sports
- Next wave of hiring focused on Tech Ops, Services, Paralympic Sport and Central Planning in buildup to Test Events

LA28 Ticketing Update



- Over 4M tickets sold across 85 countries and all 50 states in Drop 1
 - 95% of all tickets under \$100 were sold during the LA & OKC Locals Presale
 - 500k \$28 tickets sold
- Drop 2 is scheduled for Aug 2026 and will include refreshed inventory across all Olympic Sports
- Olympic Ticketing & Hospitality Request Portal closes on 18 July 2026

2026 Look Ahead



- Stakeholder service level validation ongoing, focus on Transportation, Food & Beverage and Accommodation
- Policies & Procedures workstream launched, focus on IF Travel & Per Diem, Uniform, and Food & Beverage policies in Q3 2026
- LA28 Volunteer Portal to open in Summer 2026. Major efforts across identification, development and appointment of National Technical Officials and Sport Skilled Volunteers over next 6-12 months

Key Date Reminders



- May 29, 2026: AMS (Accommodations Management System) Portal closes
- Summer 2026: LA28 Volunteer Portal Opening
- July 13, 2026: IFs to begin receiving proposed allocations from LA28 Accommodations team
- July 18, 2026: Olympic Hospitality Request Portal (HRP) and Client Ticket Portal (CTP) closes
- Q3 2026: IF Pictogram Approval Complete
- Oct 2026: VDB 3.1 Publication
- Oct 2026 at IF Forum: Finalized LA28 Sport Presentation strategy

Thank You!

